

B30 315

Customer: BHSCT Site: CAMHS Family Trauma Centre 1 Wellington Park Belfast BT9 6DJ Contact: Christine Mooney or Mark Johnson Tel: 9504 2828 ext

Track Type	Sketch	Location	Fitting Price	Price Uplift	Option List	Quantity	Width	Draw	Control side	Control Drop	K2500 Gliders White or Grey or Grey	Brackets	Fixing	Floor to track approx	Cord Tensioner	Man power	Fitting	Special Instructions	
First Floor																			
Kestrel K6200		Room 4 LR1				1	1200	Bi				Face	Face	2370		1 Man	30min	Face fix D&P top of magnets 95mm above top of baton remove old track and curtains	
Kestrel K6200		Room 4 LR2				1	1180	Bi				Face	Face	2370		1 Man	30min	Face fix D&P top of magnets 95mm above top of baton remove old track and curtains	
Kestrel K6200		Room 4 LR3				1	1190	Bi				Face	Face	2370		1 Man	30min	Face fix D&P top of magnets 95mm above top of baton remove old track and curtains	
Kestrel K6200		Room 4 LR4 viewing screen				1	1850	Bi				Face	Face	2020		1 Man	30min	Face fix D&P top of magnets 95mm above top of baton remove old track and curtains	
Kestrel K6200		Room 5 LR1				1	1200	Bi				Face	Face	2360		1 Man	30min	Face fix D&P top of magnets 95mm above top of baton remove old track and curtains	
Kestrel K6200		Room 5 LR2				1	1200	Bi				Face	Face	2360		1 Man	30min	Face fix D&P top of magnets 95mm above top of baton remove old track and curtains	
Kestrel K6200		Room 5 LR3				1	1200	Bi				Face	Face	2360		1 Man	30min	Face fix D&P top of magnets 95mm above top of baton remove old track and curtains	
Vitesse 5600W		Room 6				1	1660	Bi				Face	Face	3000		1 Man	30min	Face fix to top of brackets to top of architrave frame remove old track	
Vitesse 5600W preformed	A	Room 7 Bay				1	3895	Bi				Face	Face	2965		2 Men	30min	Face fix to top of brackets to top of architrave frame remove old track	
Vitesse 5600W preformed	A	Room 8 Bay				1	3900	Bi				Face	Face	2965		2 Men	30min	Face fix to top of brackets to top of architrave frame remove old track	
Kestrel K6200		Room 8 viewing screen				1	1860	Bi				Face	Face	2025		1 Man	30min	Face fix D&P top of magnets 95mm above top of baton remove old track and curtains	
Ground Floor																			
Vitesse 5600W preformed	A	Room 1 Bay				1	3907	Bi				Face	Face	3000		2 Men	30min	Face fix to top of brackets to top of architrave frame remove old track	
Vitesse 5600W	A	Room 1 Rear				1	1590	Bi				Face	Face	3075		1 Man	30min	Face fix to top of brackets to top of architrave frame remove old brackets	
																Parking and access 0.75hr			
Fitting Instructions																			
L2 & L3 steps																			
See special instructions column for fixing detail																			
<b>Kestrel K9500 track. Top of face fix magnet to glider hook 115mm. Top of top fix magnet to glider hook 65mm. Track profile to glider hook 42mm. If CP3 tape Bottom pocket nil heading</b>																			
<b>Trust spec track Kestrel K6200 track. Top of face fix magnet to glider hook 95mm. Top of top fix magnet to glider hook 45mm. Track profile to glider hook 30mm. If CP3 tape Middle pocket nil heading</b>																			
<b>Non magnetic Kestrel K2500 track. Face fix top of end brackets to glider hook 60mm. Top of profile to glider hook 40mm. If CP3 tape Top pocket nil heading</b>																			
Date																			

501

24/8/09

Customer		Site.										Contact.									
BHSCT		CAMHS Family Trauma Centre 1 Wellington Park Belfast BT9 6DJ										Christine Mooney or Mark Johnson									
												Tel: 95 Tel: 9504 0583 ext									
Location		Lining	Spec	Width	Single Pair	Qty	Hook drop	Pleated width	Hook position	Fitting Price	Approx Floor to track	Extra components	Tape	Heading	Stitch	Fast or loose lined	Pile	Man power	Fitting	Special Instructions	
First floor																					
Room 4 LR1		Panaz Q009 P/R 69cm width 140cm 50% fullness	FRP Col TBC		1 PR	1	1935	675	Middle		2370		Cp3	Nil	M/S	Fast	N/A	1 Man	1 Man 15min		
Room 4 LR2		Panaz Q009 P/R 69cm width 140cm 50% fullness	FRP Col TBC		1 PR	1	1935	675	Middle		2370		Cp3	Nil	M/S	Fast	N/A	1 Man	1 Man 15min		
Room 4 LR3		Panaz Q009 P/R 69cm width 140cm 50% fullness	FRP Col TBC		1 PR	1	1925	675	Middle		2370		Cp3	Nil	M/S	Fast	N/A	1 Man	1 Man 15min		
Room 4 LR4 viewing screen		Panaz Q009 P/R 69cm width 140cm 50% fullness	FRP Col TBC		1.5 PR	1	1760	1000	Middle		2020		Cp3	Nil	M/S	Fast	N/A	1 Man	1 Man 15min		
Room 5 LR1		Panaz Q009 P/R 69cm width 140cm 50% fullness	FRP Col TBC		1 PR	1	1920	675	Middle		2360		Cp3	Nil	M/S	Fast	N/A	1 Man	1 Man 15min		
Room 5 LR2		Panaz Q009 P/R 69cm width 140cm 50% fullness	FRP Col TBC		1 PR	1	1915	675	Middle		2360		Cp3	Nil	M/S	Fast	N/A	1 Man	1 Man 15min		
Room 5 LR3		Panaz Q009 P/R 69cm width 140cm 50% fullness	FRP Col TBC		1 PR	1	1915	675	Middle		2360		Cp3	Nil	M/S	Fast	N/A	1 Man	1 Man 15min		
Room 6		Panaz Q009 P/R 69cm width 140cm 50% fullness	FRP Col TBC		1 PR	1	2955	905	Middle		3000		Cp3	7mm	M/S	Fast	N/A	1 Man	1 Man 15min		
Room 7 Bay		Panaz Q009 P/R 69cm width 140cm 50% fullness	FRP Col TBC		2.5 PR	1	2570	2035	Middle		2965		Cp3	7mm	M/S	Fast	N/A	1 Man	1 Man 15min		
Room 8 Bay		Panaz Q009 P/R 69cm width 140cm 50% fullness	FRP Col TBC		2.5 PR	1	2570	2035	Middle		2965		Cp3	7mm	M/S	Fast	N/A	1 Man	1 Man 15min		
Room 8 viewing screen		Panaz Q009 P/R 69cm width 140cm 50% fullness	FRP Col TBC		1.5 PR	1	1805	1005	Middle		2025		Cp3	Nil	M/S	Fast	N/A	1 Man	1 Man 15min		
Ground Floor																					
Room 1 Bay		Panaz Q009 P/R 69cm width 140cm 50% fullness	FRP Col TBC		2.5 PR	1	2630	2040	Middle		3000		Cp3	7mm	M/S	Fast	N/A	1 Man	1 Man 15min		
Room 1 rear		Panaz Q009 P/R 69cm width 140cm 50% fullness	FRP Col TBC		1.5 PR	1	2560	1230	Middle		3075		Cp3	7mm	M/S	Fast	N/A	1 Man	1 Man 15min		
																			0.75hr parking & access		
Fitting Instructions																					
L2 steps																					
Date	work done																				

Fabric width	1500	Fabric cost	7.16	Base pricing sheet raised	1.00	Updated	1.2	Site	no	clear when actioned	ENTER ALL PRICES AT COST	only	no	disc	MAN	fabric price	carriage	filling	total	unit	Unit£	Total£						
Curt fullness	1.5	uplift	3.2	uplift	1.00	uplift	1.2	Site	no	clear when actioned	ENTER ALL PRICES AT COST	only	no	disc	MAN	fabric price	carriage	filling	total	unit	Unit£	Total£						
lining cost	1370	hem	200	hem	210	hem	210	hem	no	clear when actioned	ENTER ALL PRICES AT COST	only	no	disc	MAN	fabric price	carriage	filling	total	unit	Unit£	Total£						
excess	1.05	excess	1.05	excess	1.05	excess	1.05	excess	no	clear when actioned	ENTER ALL PRICES AT COST	only	no	disc	MAN	fabric price	carriage	filling	total	unit	Unit£	Total£						
total lining		total lining	total lining	total lining	total lining	total lining	total lining	total lining	no	clear when actioned	ENTER ALL PRICES AT COST	only	no	disc	MAN	fabric price	carriage	filling	total	unit	Unit£	Total£						
6.8	6.41	2135	5.8	5.52	2	2760	2205	Room 4 LR1	1200	1935	2	1	1	1935	1	24	24	1200	0	0	24	41.76	0	21.76	0	87.52	88	88
6.8	6.41	2135	5.8	5.52	2	2760	2205	Room 4 LR2	1180	1935	2	1	1	1935	1	24	24	1180	0	0	24	41.76	0	21.76	0	87.52	88	88
6.7	6.38	2125	5.8	5.52	2	2760	2195	Room 4 LR3	1190	1925	2	1	1	1925	1	24	24	1190	0	0	24	41.76	0	21.44	0	87.20	88	88
8.3	7.84	1980	6.6	6.21	3	2070	2030	Room 4 LR4	1850	1760	2	1.5	1.5	1760	1	24	24	1850	0	0	24	47.52	0	26.56	0	98.08	99	99
6.7	6.36	2120	5.8	5.52	2	2760	2190	Room 5 LR1	1200	1920	2	1	1	1920	1	24	24	1200	0	0	24	41.76	0	21.44	0	87.20	88	88
6.7	6.35	2115	5.8	5.52	2	2760	2185	Room 5 LR2	1200	1915	2	1	1	1915	1	24	24	1200	0	0	24	41.76	0	21.44	0	87.20	88	88
6.7	6.35	2115	5.8	5.52	2	2760	2185	Room 5 LR3	1200	1915	2	1	1	1915	1	24	24	1200	0	0	24	41.76	0	21.44	0	87.20	88	88
10	9.47	3155	7.3	6.9	2	3450	3225	Room 6	1660	2955	2	1	1	2955	1	24	24	1660	0	0	24	52.56	5	32	9	122.56	123	123
17.5	16.62	2770	18.2	17.28	5	3450	2840	Room 7	3895	2570	2	2.5	2.5	2570	1	70	70	3895	0	0	70	131.04	5	56	9	271.04	272	272
17.5	16.62	2770	18.2	17.28	5	3450	2840	Room 8 Bay	3900	2570	2	2.5	2.5	2570	1	70	70	3900	0	0	70	131.04	5	56	9	271.04	272	272
8.5	8.02	2005	8.7	8.28	3	2760	2675	Room 9 screen	1860	1805	2	1.5	1.5	1805	1	24	24	1860	0	0	24	62.64	0	27.2	0	113.84	114	114
17.8	16.98	2630	18.2	17.28	5	3450	2900	Room 1 bay	3907	2630	2	2.5	2.5	2630	1	70	70	3907	0	0	70	131.04	5	57.28	9	272.32	273	273
11.6	11.04	2760	10.9	10.38	3	3450	2830	Room 1 rear	1590	2560	2	1.5	1.5	2560	1	24	24	1590	0	0	24	78.48	5	37.12	9	153.60	154	154
131.7	124.85		122.9	116.61						Totals	13	price			price	450	894.88	23	421.4	45	1826.32							1835

Non Trust Rate


AI

Internal Use



3

Sketch A - VITASSA S600 W TRACKS

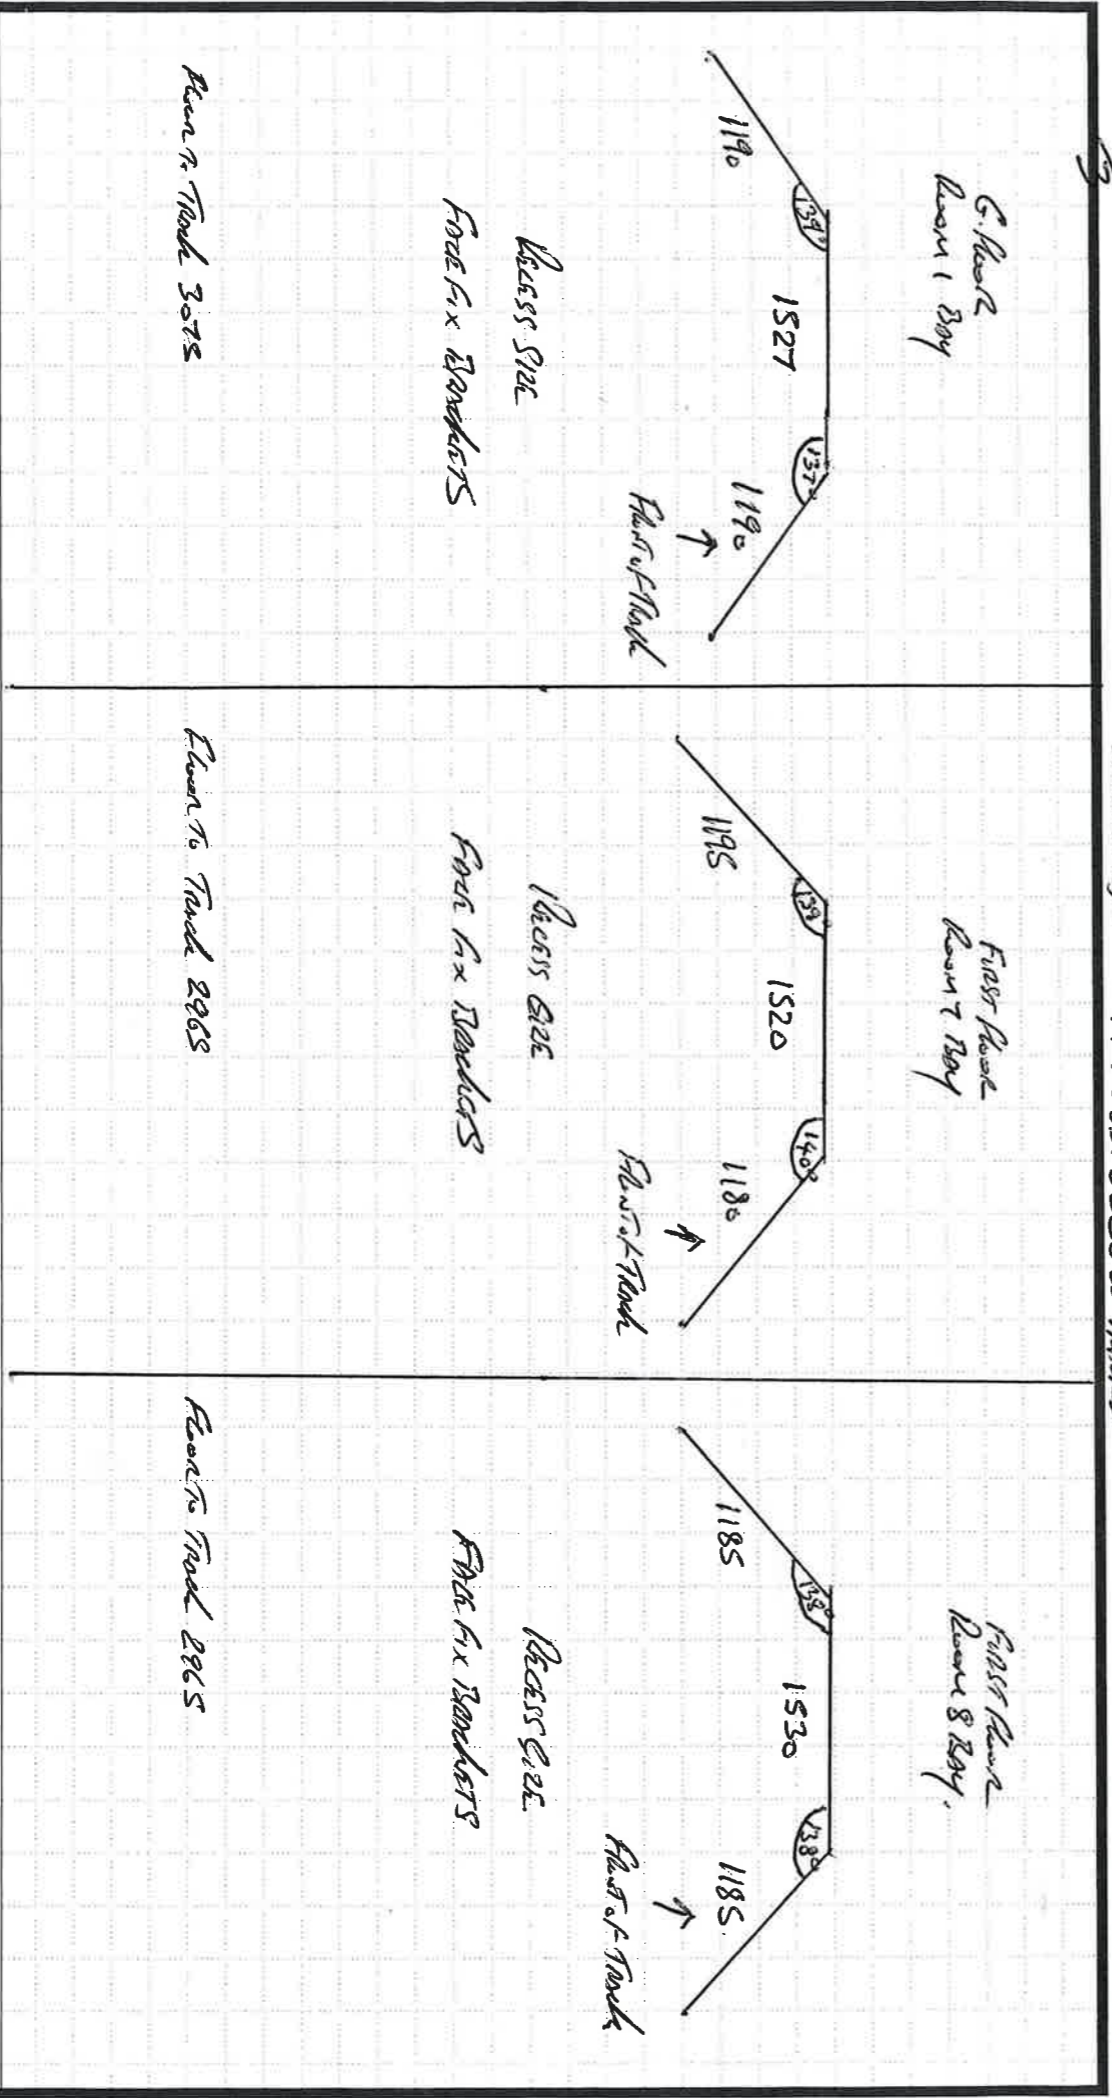

# ANDERSON INTERIORS

62-66 Duncrue Street  
 BELFAST BT3 9AY  
 Tel: (028) 9035 8000 Fax: (028) 9035 2727  
 E-mail: info@anderson-interiors.co.uk  
 www.anderson-interiors.co.uk

## AGREEMENT ON WORK TO BE DONE "BY OTHERS" ON SITE / PRODUCT LAYOUT

Drawn AD Date 24/11/25  
 Checked [Signature] Date \_\_\_\_\_  
 Customer BUSCO  
 Site CHILL'S BUNNY TOWNERS CENTRE 216/1188

Approved By \_\_\_\_\_ Date \_\_\_\_\_  
 Name Printed \_\_\_\_\_  
 Position \_\_\_\_\_  
 Company \_\_\_\_\_



**MEASUREMENT FORM** **Anderson Interiors Ltd**

<b>Date:</b> 24/11/2025	<b>Taken By:</b> Gary Buchanan	<b>Survey Date/Time:</b> 24/11/2025 11:30 / 24/11/2025 13:30	
<b>Invoice:</b> Belfast HSC Trust ( R), PO Box 1045		<b>Site:</b> CAMHS	
Ballymena		Family Trauma Ctr	
BT42 9BU		1 Wellington Pk, Belfast BT9 6DJ	
<b>Contact:</b>		<b>Contact:</b> Christine Mooney <i>Marie Johnson</i>	
<b>Tel:</b>		<b>Tel:</b> 9504 2828	
<b>Mobile:</b>		<b>Mobile:</b>	
<b>Fax:</b>		<b>Fax:</b>	
<b>Email:</b> christine.mooney@belfasttrust.hscni.net		<b>Email:</b>	
Directions Req'd: (On reverse) Yes/No		Directions Yellow: Yes/No	

**Product/Room (s) - Details:**  
 curtains for 4nr Rooms *R14, 18, 71, 65, 6* See email

*Marie Johnson confirmed H/Vent Windows ok with STD Tracks & NOT ANTI LIFTOR ALSO ok WITH C/PB TOPS WITH 3 LEADS & ZINC Hooks on ALL CURTAINS & BOY WINDOWS CURT/S FISHLINE SILLS & NOT TO FLOOR'S ESTIMATE HELP FIAP Lining ok DS PER CM.*

<b>Who makes decision:</b>	<b>When:</b>
----------------------------	--------------

**Sales Plus Points:**

<b>Any competition:</b>	<b>Quote required by:</b>
-------------------------	---------------------------

<b>No. of Fitters:</b> <i>1 Mon + 2 Weds</i>	<b>Fitting time (excl. travel):</b> <i>SEE QUOTE</i>
--	--

Extra time for Access/Parking: *3.4 hrs*

**RE-SURVEY REQUIRED:** *No.*

Planned completion date:

**Other information** *ADD TO QUOTE BOSSD and CLIMB ACCESS TO Rooms During Normal Working Hours*

**SITE INFORMATION**

<b>PARKING:</b> <i>To GET</i>	<b>Lift/Stairs:</b>
	<b>Floor (s)</b> <i>GRIST PAVES STAIRS</i>

Problem with access: *NO*

<b>POWER:</b> <i>240v</i> NONE/240V/110V/other	<b>PLANS available:</b> <i>Sketch</i>
--	---------------------------------------

**EXTRA EQUIPMENT/TOO REQUIRED:** *L2+L3 STAIRS*

**OTHER INFORMATION:**

<b>Site Condition Ready:</b> <i>Yes</i>	<b>Supervision Required:</b> <i>No</i>
---	--

**If No When:**

<b>Surveyed By:</b> <i>[Signature]</i>	<b>Date:</b> <i>24/11/25</i>
--	------------------------------
